



# PT. PJ-TEK MANDIRI

TECHNICAL INSPECTION & CERTIFICATION


|                |                                           |                     |                    |
|----------------|-------------------------------------------|---------------------|--------------------|
| Client         | : PT Pertamina EP Zona 4 Field Prabumulih | Height of Mast      | : 21,03 meter      |
| Rig ID         | : BW KB150 C                              | Hook Load           | : 34,02 ton        |
| Service        | : Service Rig                             | Power               | : 200 HP           |
| Type           | : Truck Mounted                           | Place of Inspection | : Prabumulih       |
| Manufacture    | : PT Petrodrill Manufaktur Indonesia      | Date of Inspection  | : 07 Desember 2025 |
| Year           | : 2016                                    | Rig Inspector       | : Yandi Handiyan   |
| Model / Serial | : PD30-M075-069                           |                     |                    |

## DAILY INSPECTION CAT III REPORT

| No. | Equipment                   | Deficiencies                                                                        | Categories | Remarks / Recommendation                                                                                                                           |
|-----|-----------------------------|-------------------------------------------------------------------------------------|------------|----------------------------------------------------------------------------------------------------------------------------------------------------|
| 1.  | Upper Mast                  |    | N/A        | <b>Finding</b> : N/A<br><b>MPI Result</b> : No Discontinuity<br><b>Acceptance Criteria</b> :<br>API RP 4G Sect 6.1<br><b>Total Progress</b> : 100% |
| 2.  | Base Mast                   |   | N/A        | <b>Finding</b> : N/A<br><b>MPI Result</b> : No Discontinuity<br><b>Acceptance Criteria</b> :<br>API RP 4G Sect 6.1<br><b>Total Progress</b> : 100% |
| 3.  | Raising Jack                |  | N/A        | <b>Finding</b> : N/A<br><b>MPI Result</b> : No Discontinuity<br><b>Acceptance Criteria</b> :<br>API RP 4G Sect 6.1<br><b>Total Progress</b> : 100% |
| 4.  | Pin Locking Pawl Upper Mast |  | N/A        | <b>Finding</b> : N/A<br><b>MPI Result</b> : No Discontinuity<br><b>Acceptance Criteria</b> :<br>API RP 4G Sect 6.1<br><b>Total Progress</b> : 100% |

|    |                            |                                                                                                                                                                         |          |                                                                                                                                                                                                                                                                          |
|----|----------------------------|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------|----------|--------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| 5. | Pin Locking Pawl Base Mast |                                                                                         | N/A      | <p><b>Finding :</b> N/A</p> <p><b>MPI Result :</b> No Discontinuity</p> <p><b>Acceptance Criteria :</b> API RP 4G Sect 6.1</p> <p><b>Total Progress :</b> 100%</p>                                                                                                       |
| 6. | Link Elevator              |                                                                                        | N/A      | <p><b>Finding :</b> N/A</p> <p><b>MPI Result :</b> No Discontinuity</p> <p><b>Acceptance Criteria :</b> API RP 8B Sect. 5.2.3.4</p> <p><b>Total Progress :</b> 100%</p>                                                                                                  |
| 7. | Sheave Crown Block         |                                                                                       | N/A      | <p><b>Finding :</b> N/A</p> <p><b>MPI Result :</b> No Discontinuity</p> <p><b>Acceptance Criteria :</b> API RP 8B Sect. 5.2.3.4</p> <p><b>Total Progress :</b> 100%</p>                                                                                                  |
| 8. | Frame Crown Block          |                                                                                      | N/A      | <p><b>Finding :</b> N/A</p> <p><b>MPI Result :</b> No Discontinuity</p> <p><b>Acceptance Criteria :</b> API RP 4G Sect 6.1</p> <p><b>Total Progress :</b> 100%</p>                                                                                                       |
| 9. | Hose Hydraulic             |   | Critical | <p><b>Finding :</b> Terdapat kerusakan lapisan Hose Hydraulic</p> <p><b>MPI Result :</b> N/A</p> <p><b>Acceptance Criteria :</b> API RP 4G Sect 6.1</p> <p><b>Total Progress :</b> 100%</p> <p><b>Recommendation:</b> Segera lakukan penggantian sesuai spesifikasi.</p> |



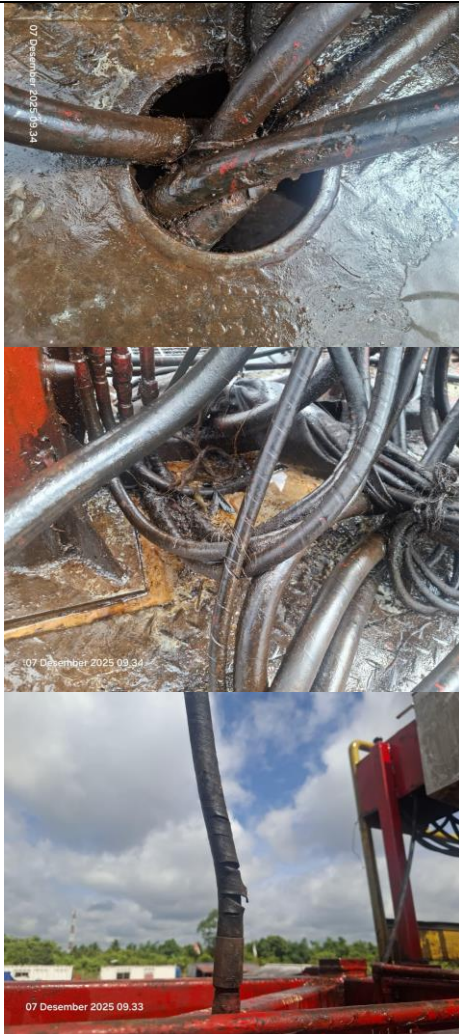

#### Result Finding Rig BW KD150C

| No.   | Category | Total Finding |
|-------|----------|---------------|
| 1.    | Major    | -             |
| 2.    | Critical | 1             |
| Total |          | 1             |

Keterangan :

1. Critical :

Kerusakan dan kegagalan peralatan dan ketidaksesuaian spesifikasi yang ditentukan sehingga dapat menyebabkan kerusakan area atau nyawa manusia. Umumnya pada wilayah komponen- Komponen yang menerima beban utama proses pengeboran.

2. Major :

Kerusakan atau kegagalan peralatan akibat ketidaksesuaian spesifikasi yang ditentukan sehingga dapat merusak peralatan utama atau menghambat operasi.

Progres pekerjaan H3 - 25% Akumulatif 65%

Dibuat oleh :

PT PJ-Tek Mandiri

Disetujui:

PT Pertamina EP Zona 4 Field Prabumulih

Yandi Handiyan
